PROJECT COMPLETION

Holton Street Bridge Rehabilitation Project

City of Milwaukee | DEPARTMENT OF PUBLIC WORKS

JULY 2026


N. Holton Street open starting July 16, 2026

Project Completion

The City of Milwaukee rehabilitated the N. Holton Street Bridge between E. Brady Street and E. Glover/Reservoir avenues. Work began in spring 2023 and was completed in summer 2026.

N. Holton Street is open to people driving, walking, and biking.


The following work took place as part of this project:

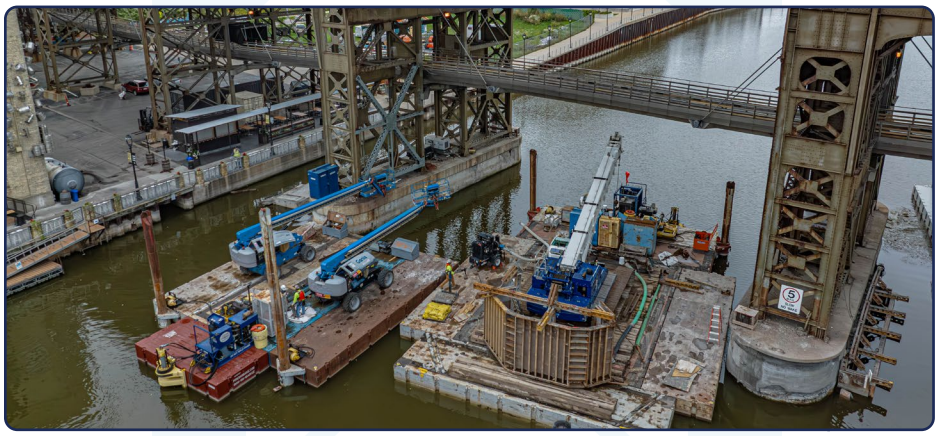

Pier Repair on N. Holton Street Bridge

2023

- Repaired piers, expansion joints, and the concrete bridge deck

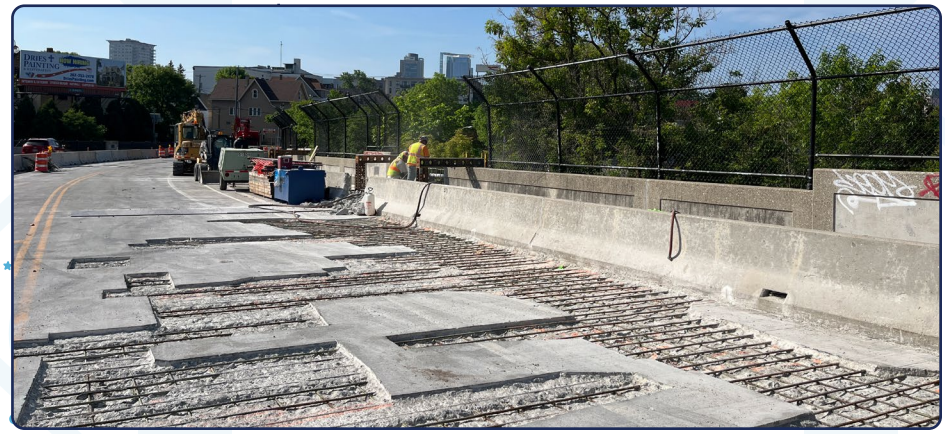

Bridge Deck Repairs on N. Holton Street Bridge



Pre-Rehabilitation on N. Holton Street Bridge


2024

- Repaired structural steel and concrete substructure
- Cleaned bridge substructure

- Began repainting bridge segments
- Repaired expansion joints



Painting Containment on N. Holton Street Bridge

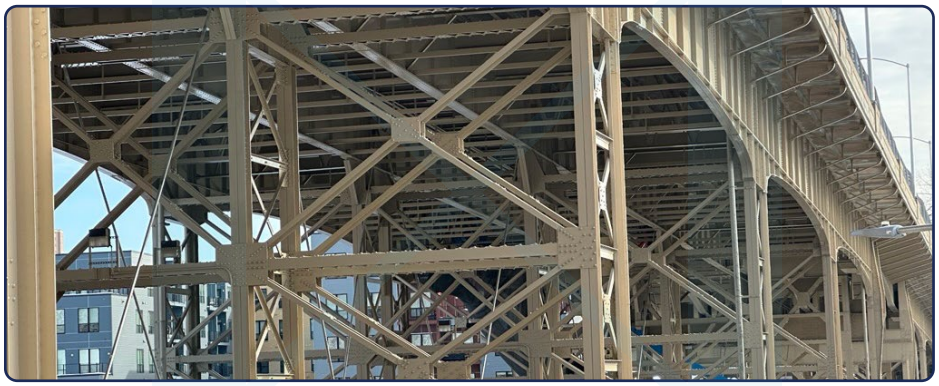


New Paint on N. Holton Street Bridge

2025

- Steel blasted old paint from the superstructure
- Repainted bridge superstructure
- Began installing new structural steel support beams

2026

- Installed new structural steel support beams

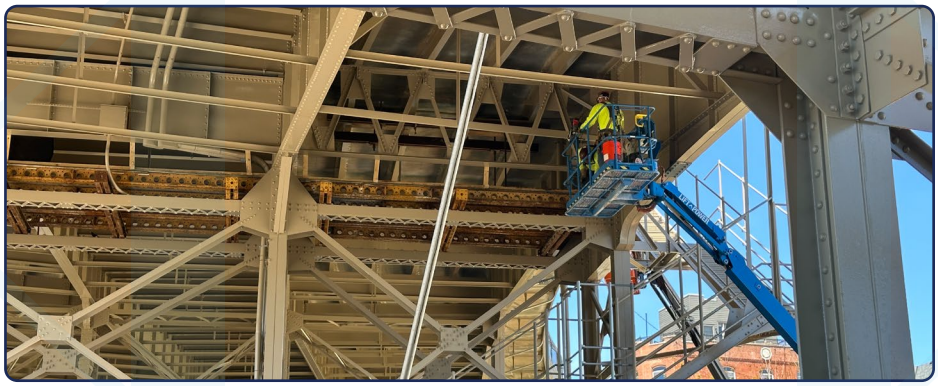

Support Beam Installation on N. Holton Street Bridge
